

Trout Creek Recreation Center, Project Report

Improvements began 1/7/2019

Total Potential

Budget

Actual

2,400,000



140,813

Percentage spent to Budget=

5.9%

Substantial Completion = **estimated early 2020**

Recent Construction Activity

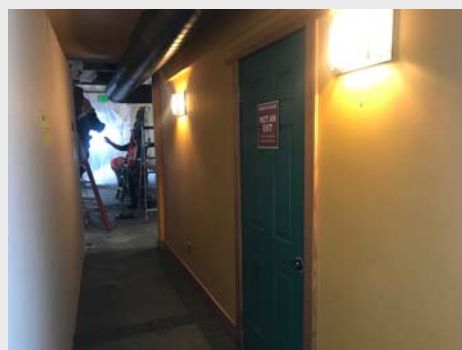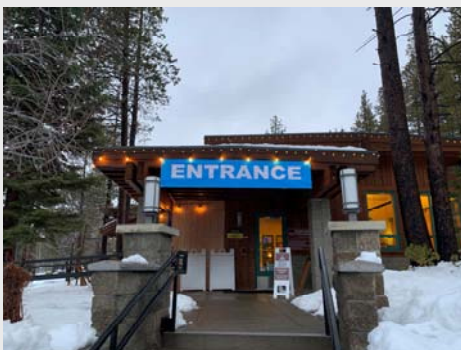

Milestones

- Signage and Communications; ongoing
- Temporary Operations; underway
- Tunnel improvements; underway
- Phase 1, estimated completion by July 4th weekend
- Phase 2, to include 670 SF of new Fitness Area
- Complete FFE installation
- Ribbon Cutting Event, TBD
